

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	
Team ID	
Project Name	ServiceNow-Based Employee Laptop Request Application
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

The work required to build the ServiceNow-Based Employee Laptop Request Application was broken down into 5 epics — Requirement Analysis & Planning, Data Architecture, Workflow Development, Security & Validation, and Testing & Deployment — each split into user stories and estimated in story points (Fibonacci scale: 1, 2, 3, 5, 8) across 4 sprints.

Sprint	Epic	USN	User Story / Task	Points	Priority
Sprint-1	Requirement Analysis & Planning	USN-1	As an analyst, I can document business objectives and functional scope for the laptop request process.	2	High
Sprint-1	Requirement Analysis & Planning	USN-2	As a developer, I can create an Update Set and a scoped Custom Application to contain all project artifacts.	1	High
Sprint-1	Data Architecture	USN-3	As a developer, I can create the Laptop Request Form table with all 9 required fields (Requester, Manager, Type, Status, Reason, etc.).	3	High
Sprint-1	Data Architecture	USN-4	As a developer, I can create a relationship linking the Laptop Request Form table to the Approval table (sysapproval_approver).	3	Medium
Sprint-1	Data Architecture	USN-5	As an employee, I can submit a laptop request through a Record Producer on the Employee Service Catalog.	3	High
Sprint-2	Workflow Development	USN-6	As the system, I can trigger a flow automatically when a new Laptop Request record is created.	2	High
Sprint-2	Workflow Development	USN-7	As the system, I can set the request Status to “Pending Approval” immediately after submission.	1	High
Sprint-2	Workflow Development	USN-8	As a manager, I can receive an approval request assigned to me with the request details.	3	High
Sprint-2	Workflow Development	USN-9	As the system, I can update Status to “Approved” and email the employee when the manager approves.	2	High
Sprint-2	Workflow Development	USN-10	As the system, I can update Status to “Rejected” and email the employee when the manager rejects.	2	High
Sprint-2	Workflow Development	USN-11	As an IT team member, I can receive a notification after approval to begin laptop provisioning.	2	Medium
Sprint-3	Security & Validation	USN-12	As the system, I can block an employee from submitting more than one laptop request per calendar year.	3	High
Sprint-3	Security & Validation	USN-13	As an admin, I can create it_manager and it_employee roles to control access.	1	High
Sprint-3	Security & Validation	USN-14	As an admin, I can create IT Managers and IT Employees groups and map users to the correct roles.	2	Medium
Sprint-3	Security & Validation	USN-15	As a manager, I can only view laptop requests (read-only access enforced by ACL).	2	High
Sprint-3	Security & Validation	USN-16	As an employee, I can create, edit, and view my own laptop requests (enforced by ACL).	2	High
Sprint-4	Testing & Deployment	USN-17	As a tester, I can verify the end-to-end submission-to-approval flow works correctly.	3	High
Sprint-4	Testing & Deployment	USN-18	As a tester, I can verify duplicate requests are blocked by the business rule with a clear error message.	2	High

Sprint	Epic	USN	User Story / Task	Points	Priority
Sprint-4	Testing & Deployment	USN-19	As a tester, I can verify email notifications are generated correctly at each stage of the workflow.	2	Medium
Sprint-4	Testing & Deployment	USN-20	As an admin, I can export the completed Update Set to XML, ready for deployment to another instance.	1	Low

Story Point Calculation Logic

Following the standard Agile definitions — a Sprint is a fixed period in which a team completes a set of tasks; an Epic is a large piece of work broken into smaller Stories; and a Story Point (Fibonacci scale: 1, 2, 3, 5, 8) represents the effort a story takes — the backlog above is broken down and summed per sprint as follows:

Sprint 1: Requirement Analysis & Planning (2+1) + Data Architecture (3+3+3) = 12

Sprint 2: Workflow Development (2+1+3+2+2+2) = 12

Sprint 3: Security & Validation (3+1+2+2+2) = 10

Sprint 4: Testing & Deployment (3+2+2+1) = 8

Total Story Points = 12 + 12 + 10 + 8 = 42 Number of Sprints = 4

Velocity = Total Story Points Completed ÷ Number of Sprints = 42 ÷ 4 = 10.5

Your team's velocity is 10.5 Story Points per Sprint.

Project Tracker, Velocity & Burndown Chart (4 Marks)

Sprint	Total Points	Duration	Start Date	End Date (Planned)	Points Completed	Release Date (Actual)
Sprint-1	12	6 Days	20 Jul 2026	25 Jul 2026	12	25 Jul 2026
Sprint-2	12	6 Days	27 Jul 2026	01 Aug 2026	12	01 Aug 2026
Sprint-3	10	6 Days	03 Aug 2026	08 Aug 2026	10	08 Aug 2026
Sprint-4	8	6 Days	10 Aug 2026	15 Aug 2026	8	15 Aug 2026

With an average sprint duration of 6 days, the team's velocity of 10.5 points per sprint equates to roughly 1.75 story points completed per day, which was used to validate that the remaining backlog was realistic for the available timeline.

Burndown Chart:

A burndown chart tracks the remaining story points against time within a sprint, making it easy to see whether the team is on pace to complete the sprint goal. The chart below shows Sprint 1 (Requirement Analysis & Data Architecture, 12 story points over 6 days), where the team tracked slightly behind the ideal pace mid-sprint before completing all planned work by day 6.

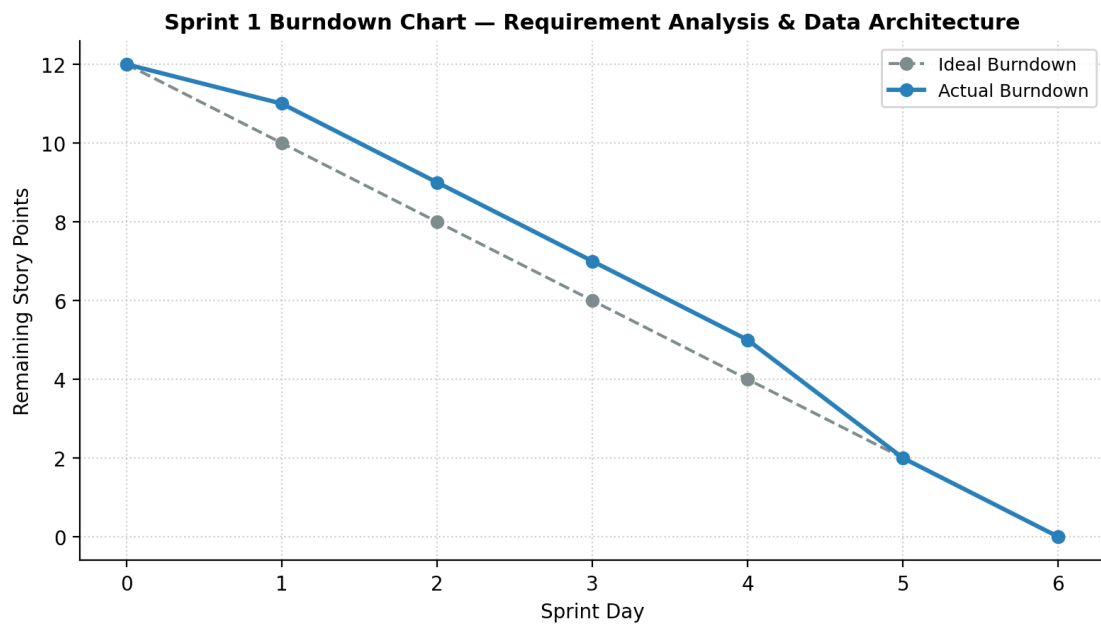


Figure 1 — Sprint 1 Burndown Chart — Requirement Analysis & Data Architecture

Reference:

<https://www.atlassian.com/agile/project-management>

<https://www.atlassian.com/agile/tutorials/epics>

<https://www.atlassian.com/agile/tutorials/sprints>

<https://www.atlassian.com/agile/project-management/estimation>

<https://www.atlassian.com/agile/tutorials/burndown-charts>
